


Reporting/cw-Linac (W. Barth, 03.09.19):

- set up of new test bunker ongoing: Recently RF-supply line prepared (RF-amplifiers => bunker); bunker roof bars delivered, mounting ongoing

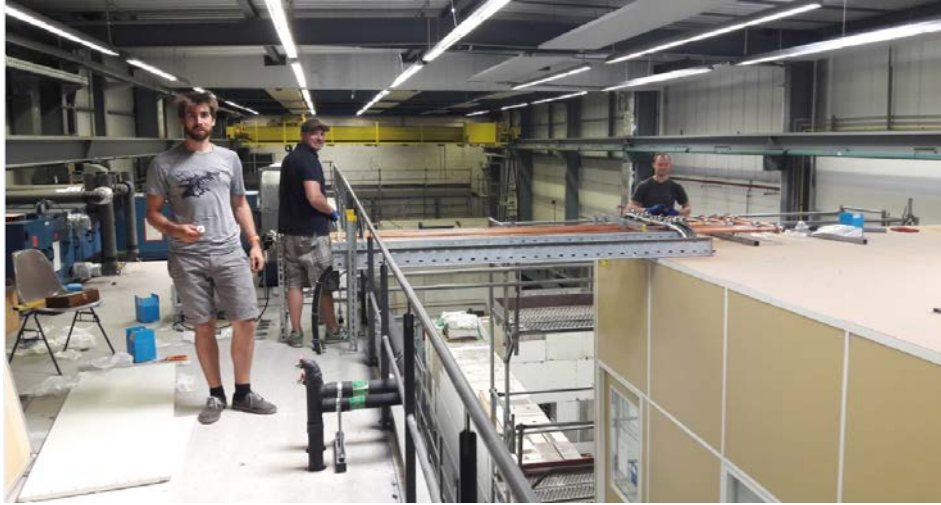

- Revised „Brandschott“ (firewall protection) design for LHe-supply line-feedthroughs specified and ordered.
- CH2 sent back to RI (waiting for RI-offer concerning new sealings and further cavity preparation, CH1: Mounting of Ti-coat => delivery to HI-Mainz planned for KW 38)
- Rf-amplifiers: tendering process due to economic reasons; restart of the process asap
- Procurement of sc solenoids ongoing
- Ultrapure Niob material for rebuncher I and II ordered.
- Waiting for additional BMBF budget for purchasing buncher I.
- Revised planning for first cold test with CH1 inside demonstrator cryostat at HI-Mainz fixed for KW38-44.
- Z-Buncher still under revision; first rf-testing performed
- GFEV for local controls of LHe-supply system already confirmed => budget confirmed (170k€).
