


Reporting/cw-Linac (W. Barth, 10.09.19):

- Time schedule/LHe-Transfer Line

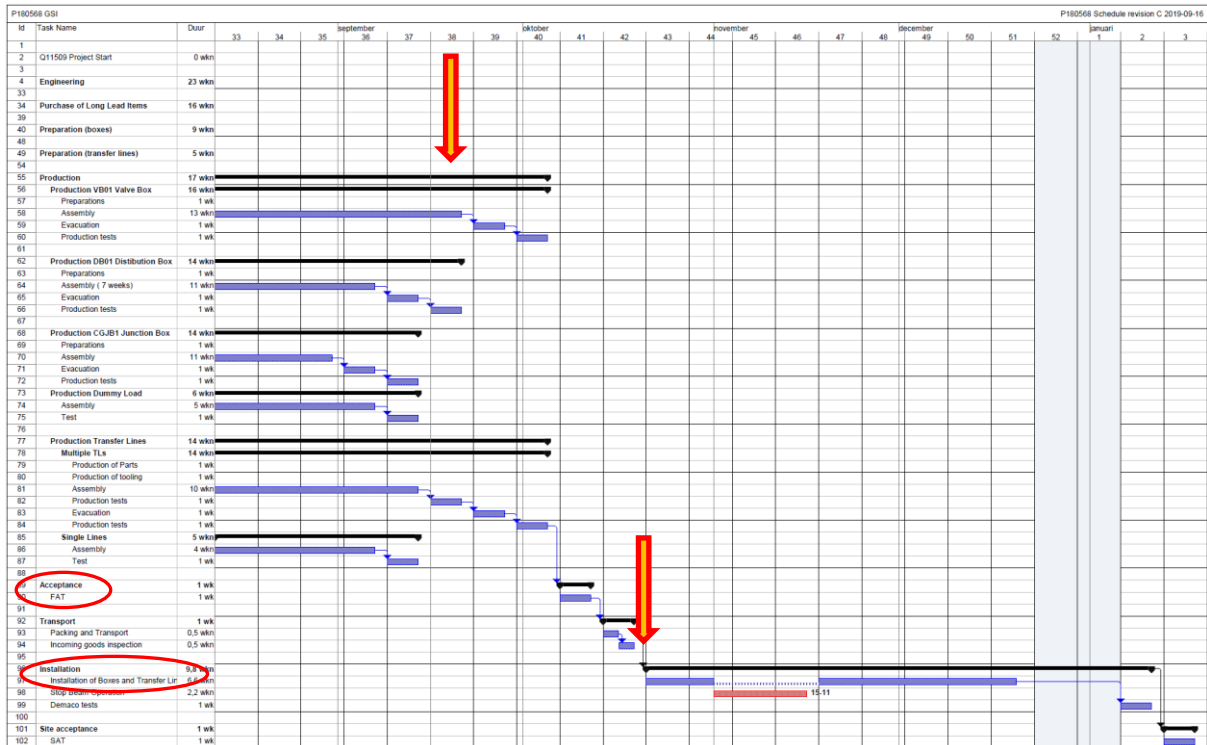

- Revised „Brandschott“ (firewall protection) design for LHe-supply line-feedthroughs still ordered, advanced suspension concept for LHe-transfer line (Baustatik-Gutachten in preparation)
- Preparation for ordering of 2nd. standard cryostat (HIM-POF4-budget)
- Preparation for ordering of 2nd. sc-rebuncher cavity (HIM-POF4-budget)
- re-call for tender for 4 rf-amplifiers (with option for additional amplifiers => POF4)
- set up of new test bunker ongoing:
 - plastering work and floor renovation (Pluhm&Zankl) already started
- RI: new sealings and further cavity preparation for CH2 ordered, CH1: Mounting of Ti-coat started => delivery to HI-Mainz planned for KW 38)
- Preparation for first cold test with CH1 inside demonstrator cryostat at HI-Mainz started
- GFEV for local controls of LHe-supply system already confirmed => budget confirmed (170k€), EBISS-Warenkorb prepared – “Einkauf”: No acceptance of unique selling point (Alleinstellungsmerkmal) => another (national tender process) => ordering earliest mid of October?! – **specification already prepared !**
- PMO: MS-Project-ressource loaded scheduling (in preparation)
