


EMC Forward Endcap Rackspace Assignment

10.12.2014



Cables through magnet
will go through both sides

- 1000 HV cables
(Enviroflex178, 1.8mm dia.)
- 24 LV cables
- Data fibres, etc.

HV cables are orderd
Need to be prepared
for right length

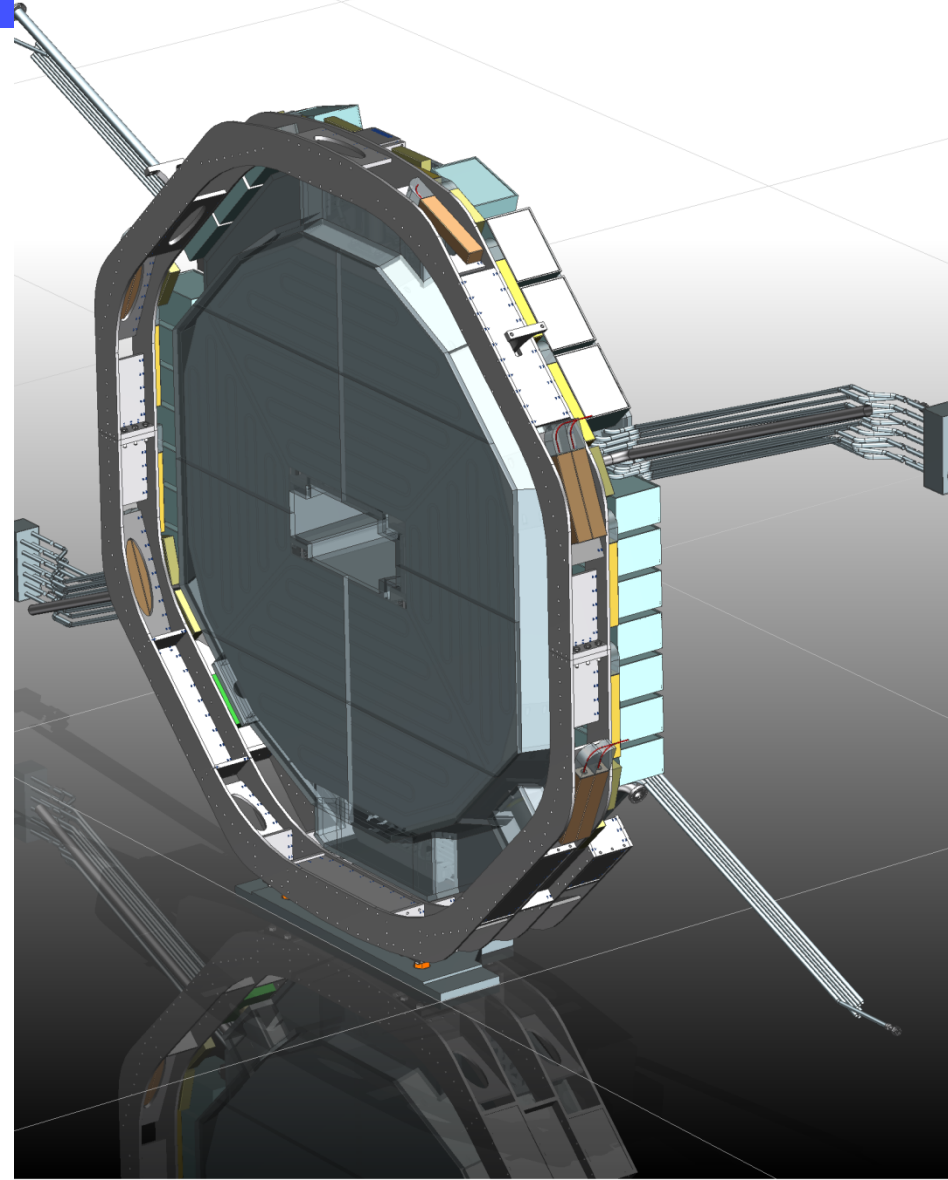

Rack Request

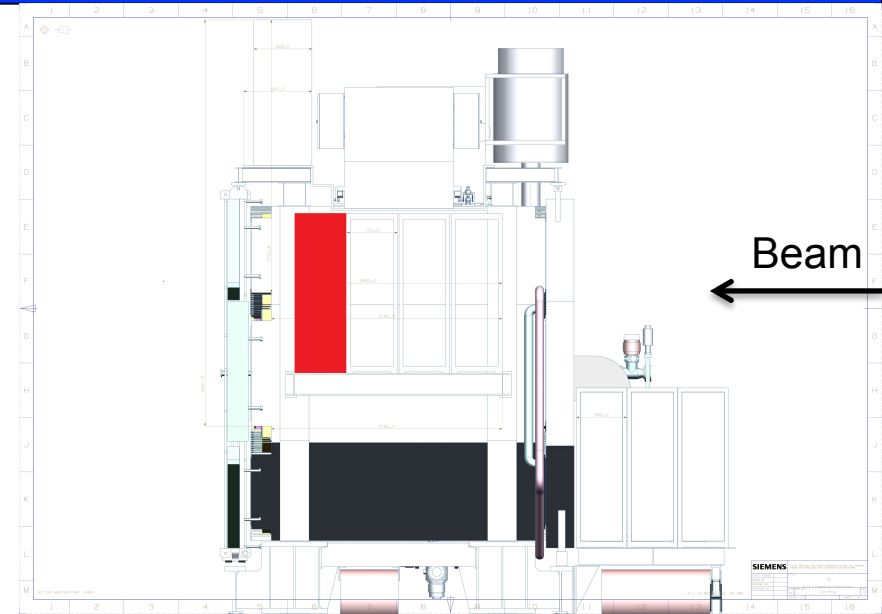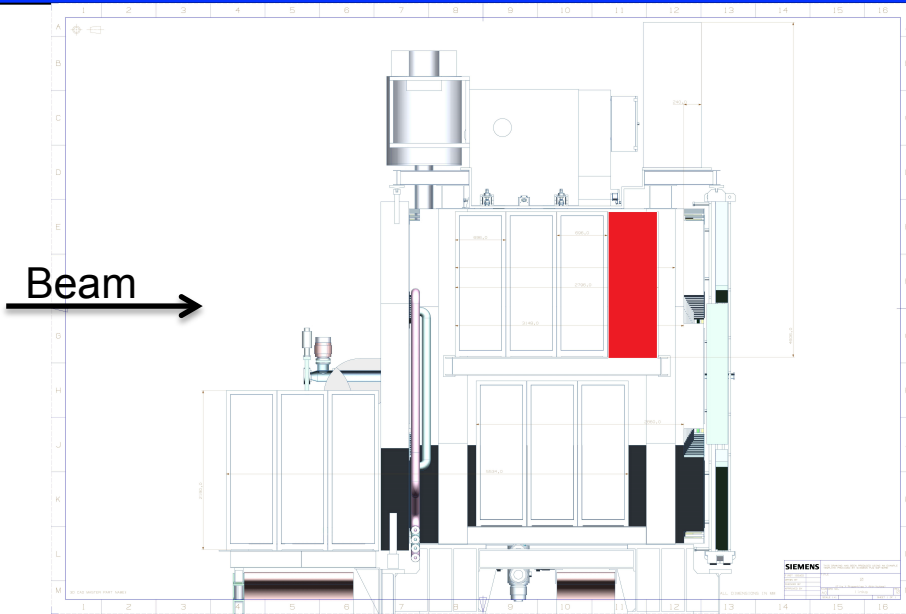

- Would like to use first racks next to forward endcap EMC
- Need about 1.8 m height on each side for patch panels and power supplies

Questions:

- Cables into rack from front or back?
- Access to backside?
- Will need meeting to discuss racks, cable trays etc.
